

15. **Approve Change Order #9 to FC-1142-00/BJC – CR 427, Phase V & VI with Bergeron Land Development, Kissimmee (\$22,949.79 + 61 day time extension).**

FC-1142-00/BJC provides for all labor, materials, equipment, coordination and incidentals necessary for the construction of approximately 1.25 miles of four lane urban roadway along an existing two lane corridor from US 17/92 to Hester Avenue (CR 427 – Phase V) and construction of approximately 2 miles of four lane urban roadway expandable to a six lane roadway along an existing two lane corridor from Hester Avenue to Lake Mary Boulevard (CR 427 – Phase VI). Change Order #9 will provide for additional roadway items required to complete the project due to conditions encountered in the field. An additional 61 days is required for the completion of this project. The following is the summary of the cost of this contract:

Original Contract Sum	\$8,145,604.69
Change Orders 1 thru 8	106,687.47
Add Change Order #9	<u>22,949.79 + 61 days</u>
Revised Contract Sum	\$8,275,241.95

Funds are available in account numbers 077515-56067000 (Engineering, Roads) and 077521-56067000 (Arterial Road Projects, Roads), CIP #DE56047Z. Public Works/Engineering Division and Fiscal Services/Purchasing and Contracts Division recommend that the Board approve and authorize the Chairman to execute the Change Order.

SEMINOLE COUNTY, FLORIDA  
CHANGE ORDER FOR CONSTRUCTION PROJECTS



Engineering Division

PURCHASING DIVISION  
(407) 321-1130

1101 E. First Street  
Sanford, FL 32771

CONTRACT NO: FC-1142-00/BJC INITIATION DATE: 06/23/03  
CHANGE ORDER NO: 09 ACCOUNT NO: \_\_\_\_\_  
CONTRACT FOR: County Road 427, Phase V & VI

ORIGINAL  
CONTRACT DATE: June 21, 2001  
ARCH/ENG PROJECT: # \_\_\_\_\_

YOU ARE REQUESTED TO MAKE THE FOLLOWING CHANGE (S) IN THIS CONTRACT:  
See Attachment A

REASON FOR CHANGE(S):  
See Attachment B

ORIGINAL CONTRACT SUM: .....	\$	<u>8,145,604.69</u>
CONTRACT SUM PRIOR TO THIS CHANGE ORDER .....	\$	<u>8,252,292.16</u>
CHANGE ORDER (increase) (decrease) (unchanged) .....	\$	<u>22,949.79</u>
NEW CONTRACT SUM INCLUDING THIS CHANGE ORDER WILL BE .....	\$	<u>8,275,241.95</u>
CONTRACT TIME WILL BE (increased) (decreased) (unchanged) .....		<u>61</u>
BY (61- ) CALENDAR DAYS .....		_____
FINAL COMPLETION DATE THROUGH THIS CHANGE ORDER .....		<u>July 31, 2003</u>

**WAIVER** This Change Order constitutes full and mutual accord and satisfaction for the adjustment of Contract Price and Time as a result of increases or decreases in costs and time of performance caused directly and indirectly from the change. Acceptance of this Waiver constitutes an agreement between COUNTY and CONTRACTOR that the Change Order represents an equitable adjustment to the Agreement and that CONTRACTOR shall waive all rights to file a Contract Claim or claim of any nature on this Change Order. Execution of this Change Order shall constitute CONTRACTOR's complete acceptance and satisfaction that it is entitled to no more costs or time (direct, indirect, impact, etc.) Pursuant to this Change Order.

**ACKNOWLEDGEMENTS** The aforementioned change, and work affected thereby, is subject to all provisions of the original Agreement not specifically changed by this Change Order, and it is expressly understood and agreed that the approval of the Change Order shall have no effect on the original agreement other than matters expressly provided herein.

NOT VALID UNTIL SIGNED BY OWNER, ARCHITECT/ENGINEER AND CONTRACTOR

\_\_\_\_\_  
Public Works/Engineering  
DEPT/DIV. Engineering  
By: STEPHEN C KIRK  
Date: 6-30-03  
By: \_\_\_\_\_

\_\_\_\_\_  
URS Corporation  
ARCHITECT/ENGINEER  
Address: \_\_\_\_\_  
1520 Tropic Park Way,  
Sanford, FL, 32773  
By: [Signature]  
Date: 6/25/03

\_\_\_\_\_  
Bergeron Land Development  
CONTRACTOR (Seal)  
2710 Michigan Ave  
Kissimmee, FL, 34744  
address: \_\_\_\_\_  
By: [Signature]  
Date: 6-24-03

Approved as to form & legal sufficiency:

\_\_\_\_\_  
County Attorney  
Date: 7/1/03

SEMINOLE COUNTY BOARD  
OF COUNTY COMMISSIONERS

ATTEST:

Daryl McLain Chairman

MARYANNE MORSE, Clerk to the Board of County  
Commissioners in and for Seminole County, Florida

BCC APPROVAL DATE: Aug. 12, 2003

DATE: \_\_\_\_\_

SEMINOLE COUNTY CHANGE ORDER # 09  
CR 427 PHASE V & VI  
CONTRACT FOR BERGERON LAND DEVELOPMENT  
CONTRACT NO.: FC-1142-00/BJC

REASON FOR CHANGE (S):

- I. Work in the area of CR-427 and SR-417 did not commence prior to obtaining a Special Permit issued by FDOT Turnpike District. The permit contained several MOT restrictions at CR-427 and SR-417. To comply with these restrictions the Contractor had to adjust his sequence of operations in the area. Twenty-eight (28) non-compensatory days be added to the contract time.
- II. A MOT change to provide continued access to local business owners and residents between Station 117+00 and Station 168+00 was required. Four (4) non-compensatory contract days be added to the contract time to complete this work.
- III. Repairs made to the City of Sanford sewerline resulted in damage to the newly placed structural asphalt. Bergeron was directed to remove the damaged area, correct with full depth limerock and 3" Structural Asphalt. Time and materials were calculated and a negotiated price of \$3,120.47 was agreed upon to complete this work. Three (3) non-compensatory days be added to the contract time to complete this work.
- IV. Seminole County requested a price to apply brick etching to the traffic separator throughout the project. The negotiated price to complete this work is \$4.10 (SF) for a total of \$9,553.00. A total of three (3) non-compensatory days be added to the contract time to complete this work.
- V. To allow continued access to residents at Elderberry Court, approximate Station 247+90 (LT), the existing driveway was removed, the area graded and a new 6" Driveway constructed. A negotiated price of \$1,274.25 to complete this work was agreed upon. A total of two (2) non-compensatory days be added to the contract time to complete this work.
- VI. The Contractor was directed to install "Bicycle" Handrail at various locations throughout the project limits for the safety of the pedestrian and traveling public. The negotiated price to complete this work is \$30.31 per linear foot, for a total of \$9,002.07.
- VII. Additional forcemain installation was required at Hester Avenue to continue service to local residents. A total of fourteen (14) non-compensatory days be added to the contract time to complete this work.
- VIII. Per Contract Documents, Bergeron requested Memorial Day (May 24, 25 and 26, 2003) and Independence Day (July 4, 5 and 6, 2003) as Holiday Time suspension. A total of six (6) non-compensatory days will be added to the contract time.
- IX. Due to inclement weather during the Month of April 2003 one (1) non-compensatory day will be added to the contract per the Contract Specifications.



# BERGERON

LAND DEVELOPMENT

15

2710 Michigan Avenue  
Kissimmee, FL 34744  
Office (407) 932-1610  
Fax (407) 932-0465

Human Resources: (407) 518-4954  
Maintenance: (407) 518-0133

June 3, 2003

URS Corporation  
1520 Tropic Park Drive  
Sanford, FL 32773

Re: Seminole County FC-1142-00/BCJ  
CR-427 Phase V & VI  
(SR 600/US 17-92 to 417 Expressway)

Attn: Charles J. Sukanek P.E.

Subject: **Contract Time**

Dear Sir,

As discussed at our weekly meeting, BLD has reviewed the contract days and propose the following for final distribution of contract time. BLD requests these days be added to the final change order.

1. Current Final Completion through C.O. #7		May 30, 2003
2. Ltr # 118 & Ltr # 120	32 days	July 1, 2003
3. Memorial Holiday	3 days	July 4, 2003
4. 4th of July Holiday	3 days	July 7, 2003
5. Sunland repairs	3 days	July 10, 2003
6. Drive at Elderberry Court	2 days	July 12, 2003
7. Misc. rain (May)	2 days	July 14, 2003
8. Etch traffic separators	3 days	July 17, 2003
9. FM at Hester Ave.	14 days	July 31, 2003

This is the final time request unless any last minute additions or changes are made to contract work tasks. If you should have any questions on this matter, please feel free to contact me.

Sincerely,  
Bergeron Land Development, Inc.

Carmine Restino  
Project Manager

BLD/124/Ltr129

RECEIVED

JUN - 2 2003

URS - SANFORD  
CR 427 OFFICE

Item

Description

**Additional Time and Money to  
Close-Out Project CR427**

	Bergeron Days	Bergeron Money	URS Days	URS Money
Lt 118 MOT Flea World	4	\$0.00	4	\$0.00
Lt 119 Limerock Trucking	8	\$3,714.00	0	\$0.00
Lt 120 SR417 MOT	28	\$4,489.75	28	\$0.00
Memorial Holiday	3	\$0.00	3	\$0.00
4th Of July Holiday	3	\$0.00	3	\$0.00
Lt 130 Sunland Repair	3	\$3,325.58	3	\$3,120.47
Lt 128 Eldreberry Driveway	2	\$1,420.11	2	\$1,274.25
Misc. Rain (May)	2		1	
Etch Traffic Seperator	3		3	
Lt 133 Hester FM	14		14	
<b>Total</b>	<b>70</b>	<b>\$12,949.44</b>	<b>61</b>	<b>\$4,394.72</b>
<b>Difference</b>			<b>9</b>	<b>-\$8,554.72</b>
<b>Agreed Total</b>			<b>61</b>	<b>\$4,394.72</b>

MAY 30  
 30  
 JUNE 30  
 31  
 July 31  
 } 61 May

final July 31  
 submit to June 30

OK  
 CPM  
 6/5/03

# BERGERON

LAND DEVELOPMENT

15

2710 Michigan Avenue  
Kissimmee, FL 34744  
Office (407) 932-1610  
Fax (407) 932-0465

Human Resources: (407) 518-4954  
Maintenance: (407) 518-0133

May 8, 2003

URS Corporation  
1520 Tropic Park Drive  
Sanford, FL 32773

Re: Seminole County FC-1142-00/BCJ  
CR-427 Phase V & VI  
(SR 600/US 17-92 to 417 Expressway)

Attn: Charles J. Sukanek P.E.

Subject: **MOT at SR 417**

Dear Sir,

Seminole Co. Purchasing Dept. received competitive bids for project FC-1142-00/BJC (CR 427 Ph. V & VI) on March 9, 2001. BLD entered into the contract with Seminole Co. on June 21, 2001 and a Notice to Proceed was issued. BLD began work on July 9, 2001. Subsequently, BLD submitted for approval the MOT plan as stipulated in the contract documents. After the first submittal, a few corrections and modifications took place and a final MOT plan was established. This plan was the overall guide on the logic to build the new road while maintaining traffic on existing CR 427.

Through all the correspondence to prospective bidders and through all meetings prior to and up to the NTP and the detailed planning for the maintenance of traffic no mention of a "special permit" issued by the FDOT Turnpike District was brought to the attention on BLD. The restrictions of work areas and lane widths specified in the "special permit" conflicted with the logic BLD put forth in the MOT plan submitted (see sheet 29). It was not until Feb. 19, 2002 (days past the NTP) that this "special permit" was issued to BLD and became the strict rules for building the area governed not by the plans provided BLD but by the doctrines of the "special permit." If in fact BLD had knowledge of this "special permit" prior to bidding the MOT costs and time stipulated would have been greater in BLD's original bid.

BLD/124/Ltr120


RECEIVED  
MAY -8 2003

URS - SANFORD  
CR 427 OFFICE

2

Therefore, attached is a reasonable estimate of what BLD expects to be compensated for having to comply with the restrictions that were not known at the time of bid. If you should have any questions on this matter, please feel free to contact me.

Sincerely,  
Bergeron Land Development, Inc.

A handwritten signature in black ink, appearing to read 'Carmine Restino', written over the printed name.

Carmine Restino  
Project Manager



# BERGERON

LAND DEVELOPMENT

15

2710 Michigan Avenue  
Kissimmee, FL 34744  
Office (407) 932-1610  
Fax (407) 932-0465

Human Resources: (407) 518-4954  
Maintenance: (407) 518-0133

May 7, 2003

URS Corporation  
1520 Tropic Park Drive  
Sanford, FL 32773

Re: Seminole County FC-1142-00/BCJ  
CR-427 Phase V & VI  
(SR 600/US 17-92 to 417 Expressway)

Attn: Charles J. Sukanek P.E.

Subject: **MOT Change (Time Extension)**

Dear Sir,

Prior to the mainline traffic switch from sta. 117+0 to 168+0 BLD submitted the traffic configuration in this area and it was approved. After the traffic switch, Seminole Co. directed BLD to change the approved configuration and move the traffic crossover to Thomas Stable Road because of traffic at the rear entrance to Flea World. This move worked out well for the customers of Flea World and the traveling public in general. BLD did this at no additional cost to the contract. However, time for this additional MOT work and paving was not addressed. BLD requests four (4) additional contract days be added to the contract time as well as full compensation for this matter. If you should have any questions on this matter, please feel free to contact me.

Sincerely,  
Bergeron Land Development, Inc.

  
Carmine Restino  
Project Manager

BLD/124/Ltr118

**RECEIVED**  
MAY 7 8 2003

URS - SANFORD  
CR 427 OFFICE

# BERGERON

LAND DEVELOPMENT

**15**

2710 Michigan Avenue  
Kissimmee, FL 34744  
Office (407) 932-1610  
Fax (407) 932-0465

Human Resources: (407) 518-4954  
Maintenance: (407) 518-0133

May 28, 2003

URS Corporation  
1520 Tropic Park Drive  
Sanford, FL 32773

Re: Seminole County FC-1142-00/BCJ  
CR-427 Phase V & VI  
(SR 600/US 17-92 to 417 Expressway)


Attn: Charles J. Sukanek P.E.

Subject: **Corrections - Sunland Dr.**

Dear Sir,

BLD is in the process of correcting the road crossing done by the City of Sanford. This road crossing did not meet current compaction standards. BLD plans to use full depth limerock and 3" asphalt structure to bring this area into specification. Costs will be monitored and reasonable compensation for this work will be expected. If you should have any questions on this matter, please feel free to contact me.

Sincerely,  
Bergeron Land Development, Inc.



Carmine Restino  
Project Manager

**RECEIVED**  
MAY 28 2003

URS - SANFORD  
CR 427 OFFICE

BLD/124/Ltr127

**BERGERON**  
LAND DEVELOPMENT  
OF CENTRAL FLORIDA INC.

**15**

2710 Michigan Avenue  
Kissimmee, FL 34744  
Office (407) 932-1610

Fax Number:  
(407) 932-0465

May 29, 2003

URS Corporation  
1520 Tropic Park Drive  
Sanford, FL 32773

Re: Seminole County FC-1142-00/BCJ  
CR-427 Phase V & VI  
(SR 600/US 17-92 to 417 Expressway)

Attn: Charles J. Sukanek P.E.

Subject: Sunland Dr.

Dear Sir,

URS through directive from Seminole Co. has instructed BLD to repair a road crossing done by the City of Sanford (see BLD Ltr # 127). Attached is the price for this repair. BLD requests three additional contract days be added for this work task. If you should have any questions on this matter, please feel free to contact me.

Sincerely,  
Bergeron Land Development, Inc.

  
Carmine Restino  
Project Manager

**RECEIVED**  
MAY 29 2003

URS - SANFORD  
CR 427 OFFICE

BLD/124/Ltr130

[illegible]

# Sunland Drive Utility Correction

	BLD Original Days Requested	Agreed Days Requested	BLD Original Total Price	Agreed Total Price
Sunland Drive	3	3	\$ 3,325.58	\$ 3,120.47
Difference		0		-\$205.11
Total Agreed		3		\$3,120.47

OK  
com  
6/5/03

**RECEIVED**

JUN 10 2003

URS - SANFORD  
CR 427 OFFICE

# BERGERON

LAND DEVELOPMENT

15

2710 Michigan Avenue  
Kissimmee, FL 34744  
Office (407) 932-1610  
Fax (407) 932-0465

Human Resources: (407) 518-4954  
Maintenance: (407) 518-0133

April 16, 2003

URS Corporation  
1520 Tropic Park Drive  
Sanford, FL 32773

Re: Seminole County FC-1142-00/BCJ  
CR-427 Phase V & VI  
(SR 600/US 17-92 to 417 Expressway)

Attn: Charles J. Sukanek P.E.

Subject: **Traffic Separator Etching**

Dear Sir,

Attached is the price you requested for traffic separator etched. If you should have any questions on this matter, please feel free to contact me.

Sincerely,  
Bergeron Land Development, Inc.



Carmine Restino  
Project Manager

BLD/124/Ltr116

RECEIVED

APR 16 2003

URS - SANFORD  
CR 427 OFFICE

DESCRIPTION	QUANTITY	UNIT	no	Rate/Hour	Man Hours	Extension
etching traffic seperators	3308	sf				
Total Labor	\$0.00					\$0.00
Total Material	\$0.00					\$0.00
Total Equipment	\$0.00					\$0.00
Total Subcontractor	\$13,546.26					\$0.00
Total Job Cost	\$13,546.26					\$0.00
Total Cost	\$13,546.26					\$0.00
Unit Price	\$4.10					\$0.00
Seminole County requested etching traffic seperators						\$0.00
Labor Burden @ 44%						\$0.00
Labor Profit @ 15%						\$0.00
Total Labor /Burden /Profit						\$0.00
Materials						\$0.00
Qty						\$0.00
Unit Price						\$0.00
Extension						\$0.00
Total Materials Cost						\$0.00
State sales Tax @ 7%						\$0.00
Materials Profit @ 15%						\$0.00
Total Material /Tax / Profit						\$0.00
Sub Contract						\$0.00
decorative concrete systems						\$0.00
Amount						\$0.00
3308 sf						\$0.00
Unit Price						\$0.00
\$3.90						\$0.00
Extension						\$0.00
Total						\$0.00
Markup 5%						\$0.00
Total Sub-contract						\$0.00
Equipment						\$0.00
Quantity						\$0.00
Unit Price						\$0.00
Extension						\$0.00
Total Equipment Cost						\$0.00
Profit @ 15 %						\$0.00
Total Equipment / Profit						\$0.00

April 28, 2003

Stephen C. Krug  
Seminole County Engineering  
520 W. Lake Mary Blvd., Suite 200  
Longwood, Fl., 32750

RE: Seminole County Road 427, Phase V and VI  
Seminole County Project FC-1142-00/BJC  
Subject: Etching Traffic Separator  
URS Letter: 0234

Dear Mr. Krug:


Seminole County requested Bergeron submit a price to apply brick etching to traffic separator throughout the project.

After reviewing the pricing, URS finds the price submitted by Bergeron Land Development of \$4.10 per square foot to be fair and reasonable for the completion of this work. We recommend approval of this amount and will incorporate it into a future change order if you concur.

If you have any questions or require additional information please feel free to contact me.

SINCERELY,

URS CORPORATION

  
Charles J. Sukanek, P.E.,  
Resident Engineer

Attachments

CJS/jjc

CC: Timothy Thacker  
File

URS Corporation



# BERGERON

LAND DEVELOPMENT

15

2710 Michigan Avenue  
Kissimmee, FL 34744  
Office (407) 932-1610  
Fax (407) 932-0465

Human Resources: (407) 518-4954  
Maintenance: (407) 518-0133

April 16, 2003

URS Corporation  
1520 Tropic Park Drive  
Sanford, FL 32773

Re: Seminole County FC-1142-00/BCJ  
CR-427 Phase V & VI  
(SR 600/US 17-92 to 417 Expressway)

Attn: Charles J. Sukanek P.E.

Subject: **Traffic Separator Etching**

Dear Sir,

Attached is the price you requested for traffic separator etched. If you should have any questions on this matter, please feel free to contact me.

Sincerely,  
Bergeron Land Development, Inc.

  
Carmine Restino  
Project Manager

BLD/124/Ltr116

RECEIVED

APR 16 2003

URS - SANFORD  
CR 427 OFFICE

[illegible]

Job \_\_\_\_\_ Project No. \_\_\_\_\_  
Description TRAFFIC SEPARATOR Computed by \_\_\_\_\_  
SQUARE FOOTAGE - Etching Checked by \_\_\_\_\_

Page \_\_\_\_\_ of \_\_\_\_\_  
Sheet \_\_\_\_\_ of \_\_\_\_\_  
Date \_\_\_\_\_  
Date \_\_\_\_\_

Reference

$$(417) \quad 325' \times 2.5' W = 812.5$$

(BEDFORD)


$$121' \times 2.5' W = 302.5$$

(17-92)

$$486' \times 2.5' W = 1215.0$$

---

$$\text{TOTAL} \quad 2330 \text{ ft}^2$$

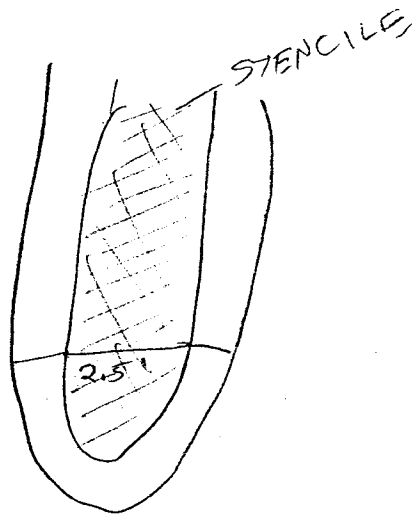

# BERGERON

LAND DEVELOPMENT

15

2710 Michigan Avenue  
Kissimmee, FL 34744  
Office (407) 932-1610  
Fax (407) 932-0465

Human Resources: (407) 518-4954  
Maintenance: (407) 518-0133

May 28, 2003

URS Corporation  
1520 Tropic Park Drive  
Sanford, FL 32773

Re: Seminole County FC-1142-00/BCJ  
CR-427 Phase V & VI  
(SR 600/US 17-92 to 417 Expressway)


Attn: Charles J. Sukanek P.E.

Subject: Driveway at Elderberry Court

Dear Sir,

Attached is the price to remove and grade the driveway at Elderberry Court. The concrete drive will be placed by the contract price for concrete sidewalk 6" thick (item 522-2). BLD also requests two contract days be added to the contract. If you should have any questions on this matter, please feel free to contact me.

Sincerely,  
Bergeron Land Development, Inc.



Carmine Restino  
Project Manager

RECEIVED

MAY 28 2003

URS - SANFORD  
CR 427 OFFICE

BLD/124/Ltr128



## Elderberry Court Driveway Modification

	BLD Original Days Requested	Agreed Days Requested	BLD Original Total Price	Agreed Total Price
Elderberry Driveway	2	2	\$ 1,420.11	\$ 1,188.25
Difference		0		-\$231.86
Total Agreed		2		\$ 1,274.25

OK  
COM  
6/2/03

## 15

TO: URS

DATE	5/06/03	JOB NO.	124
ATTENTION	CHUCK SUKAMEL		
RE:	CR 427 PH I; PH VI SEMINOLE Co.		

☐ \_\_\_\_\_

[illegible]

☐ \_\_\_\_\_

☐ PRINTS RETURNED AFTER LOAN TO US

REMARKS \_\_\_\_\_

RECEIVED  
MAY - 6 2003

~~URS - SANFORD~~  
~~CR 427 OFFICE~~

COPY \_\_\_\_\_

**SIGNED:**

If enclosures are not as noted, kindly notify us at once





15

Part/Description

Sub Amount



# ONSITE SERVICES

of Mid-Florida, Inc.



**FIELD RECONDITIONING**  
**MOBILE WELDING FABRICATION**

Phone: 386/736-4227  
 Mobile: 407/444-2951

265 Damascus Road  
 Deland, FL 32724

NAME

BERGERON LAND DEVELOPMENT

REPAIR ORDER

ADDRESS

2710 MICHIGAN AV

CITY

KISSIMMEE, FL

PHONE

407-688-7184 Fax: 407-688-7079

ESTIMATE ON HANDRAIL S.R.427

TERMS

## REPAIR ORDER - DESCRIPTION OF WORK

Fabricate and install aluminum handrail  
 as per section 516 of the standard specifications

1 @ 112LF 3 rail 27'00" + 17'00" = 44'00" 28'75"

1 @ 35LF 3rail 28'00 per ft. 3rail 27'00"

1 @ 45LF 2rail 21'50" + 4'00" 21.50 per ft. 2rail 22'90"

1 @ 43LF 2rail 22'90"

1 @ 51LF 2rail 22'90"

1 @ 58LF 2rail 22'90"

1 @ 205LF 3rail 28'76"

DATE

4-24-03

UNIT

CHART

TOTAL LABOR

15 07984

TOTAL PARTS

PAINT

SUBLET REPAIRS

MISC. MERCHANDISE

MISC. MERCHANDISE

I hereby authorize the above repair work to be done along with necessary incident's. You and your employees may operate above equipment for purposes of testing inspection or delivery of my risk. I request that you acknowledge on above equipment to secure the official of reports like etc.

It is understood that this company assumes no responsibility for loss or damage by theft or fire to equipment placed with them for storage, sale, repair or while road testing.

SIGNED

TOTAL

TAX

TOTAL

SEE BACK FOR

TOTAL PARTS &gt;

14634.82

Florida Department of Transportation

Trns\*port xxx

Item Average Unit Cost

From 2002/01/01 to 2002/11/18  
Contract Type: CC STATEWIDE  
From: 0050 To: 1999999999

Item	No. of Conts	Weighted Average	Total Amount	Total Quantity	Unit Meas	Obs?	Description
0508 73 3					LF	N	SUBMARINE CABLE ASSEMBLY (INSTALL)
0508 73 4					LF	N	SUBMARINE CABLE ASSM(REMOVE)
0508 76 1					LS	N	SPAN MOTORS & AUXILIARIES(FURNISH & I)
0508 76 3					LS	N	SPAN MOTORS & AUXILIARIES(INSTALL)
0508 76 4					LS	N	SPAN MOTORS & AUXILIARIES(REMOVE)
0508 76 5					LS	N	SPAN MOTORS & AUXILIARIES(RECONDICTION)
0508 77 1					EA	N	LOGIC CONTROLLER (PROGRAMMABLE)
0508 77 4					EA	N	LOGIC CONTROLLER (PROGRAMMABLE) (REMOVE)
0508 77 5					EA	N	LOGIC CONTROLLER (PROGMABLE) (PROGMING)
0508 78 1					LS	N	LIMIT SWITCHES & TRANSDUCERS (F&I)
0508 78 4					LS	N	LIMIT SWITCHES & TRANSDUCERS(REMOVE)
0508 79 1					EA	N	CONTROL CONSOLE (F&I)
0508 79 4					EA	N	CONTROL CONSOLE (REMOVE)
0508 80 1					EA	N	BRAKE SYSTEM (F&I)
0508 80 4					EA	N	BRAKE SYSTEM (REMOVE)
0508 81 1					EA	N	SWITCHES (LIMIT & SEATING) (F&I)
0508 82 1					EA	N	CONTROL PANEL/MOTOR CONTROLLER (F&I)
0508 82 4					EA	N	CONTROL PANEL/MOTOR CONTROLLER (RECOND)
0508 82 5					EA	N	CONTROL PANEL/MOTOR CONTROLLER (REPLACE)
0508 83103					AS	N	MOVABLE BR INTGR DR SYS(F&I) (41-60 KW)
0508 83106					AS	N	MOVABLE BR INTGR DR SYS(116 - 155 KW)
0508 83107					AS	N	MOVABLE BR INTGR DR SYS(156 - 190 KW)
0509 80 1					LS	N	ELECTRICAL SYSTEM (F&I) (TEMPORARY)
0509 80 4					LS	N	ELECTRICAL SYSTEM (REMOVE) (TEMPORARY)
0510 1					LS	N	NAVIGATION LIGHTS
0510 1 3					EA	N	NAVIGATION LIGHTS (PIERS)
0512 1					LS	N	CONTROL HOUSE
0512 1 1					LS	N	CONTROL HOUSE (RENOVATION)
0512 71 1					EA	N	MOVABLE BRIDGE PLUMBING SYSTEM
0514 71 1	1	\$2.14	\$20,013.28	9,352.000	SY	N	PLASTIC FILTER FABRIC (SUBSURFACE)
0514 71 2	1	\$1.85	\$3,459.50	1,870.000	SY	N	PLASTIC FILTER FABRIC (STABILIZATION)
0514 72	3	\$5.90	\$92,755.50	15,731.000	SY	N	LINER IMPERMEABLE PVC
0515 1 1	4	\$34.54	\$54,296.40	1,572.000	LF	N	PIPE HANDRAIL (STEEL)
0515 1 2	9	\$23.40	\$88,974.53	3,803.000	LF	N	PIPE HANDRAIL (ALUMINUM)
0515 1 3					LF	N	PIPE HANDRAIL (STEEL, BRIDGE)
0515 1 4					LF	N	PIPE HANDRAIL (ALUMINUM, BRIDGE)
0515 1 5	1	\$37.45	\$15,803.90	422.000	LF	N	PIPE HANDRAIL (PVC)
0515 2101	1	\$78.00	\$9,828.00	126.000	LF	N	PED/BICYCLE RAILING (NS) 42" PICKET RAIL
0515 2202	1	\$58.60	\$24,377.60	416.000	LF	N	PED/BICYCLE RAILING (STL) 54" PICKET RAIL
0515 2301	4	\$49.98	\$148,132.61	2,964.000	LF	N	PED/BICYCLE RAILING (ALUM) 42" PICKET RAIL
0515 2302	1	\$49.00	\$56,056.00	1,144.000	LF	N	PED/BICYCLE RAILING (ALUM) 54" PICKET RAIL

Florida Department of Transportation  
Tms\*port xxx  
Item Average Unit Cost

From 2001/01/01 to 2002/05/01  
Contract Type: CC STATEWIDE  
From: 0050 To: 199999999

Item	No. of Conts	Weighted Average	Total Amount	Total Quantity	Unit Meas	Obs?	Description
0508 77 1	1				EA	N	LOGIC CONTROLLER (PROGRAMMABLE)
0508 77 4					EA	N	LOGIC CONTROLLER (PROGRAMMABLE) (REMOVE)
0508 77 5	1	\$20,000.00	\$20,000.00	1.000	EA	N	LOGIC CONTROLLER (PROGRAMMABLE) (PROGMIN)
0508 78 1	2	\$7,283.00	\$21,849.00	3.000	LS	N	LIMIT SWITCHES & TRANSDUCERS (F&I)
0508 78 4					LS	N	LIMIT SWITCHES & TRANSDUCERS (REMOVE)
0508 79 1	1	\$32,500.00	\$65,000.00	2.000	EA	N	CONTROL CONSOLE (F&I)
0508 79 4					EA	N	CONTROL CONSOLE (REMOVE)
0508 80 1	2	\$9,987.50	\$159,800.00	16.000	EA	N	BRAKE SYSTEM (F&I)
0508 80 4					EA	N	BRAKE SYSTEM (REMOVE)
0508 81 1	1	\$950.00	\$15,200.00	16.000	EA	N	SWITCHES (LIMIT & SEATING) (F&I)
0508 82 1	1	\$23,750.00	\$95,000.00	4.000	EA	N	CONTROL PANEL/MOTOR CONTROLLER (F&I)
0508 82 4	1	\$34,168.00	\$34,168.00	1.000	EA	N	CONTROL PANEL/MOTOR CONTROLLER (RECOND)
0508 82 5					EA	N	CONTROL PANEL/MOTOR CONTROLLER (REPLACE)
0508 83106					AS	N	MOVABLE BR INTGR DR SYS (116 - 155 KW)
0508 83107					AS	N	MOVABLE BR INTGR DR SYS (156 - 190 KW)
0509 80 1	1	\$15,000.00	\$30,000.00	2.000	LS	N	ELECTRICAL SYSTEM (F&I) (TEMPORARY)
0509 80 4					LS	N	ELECTRICAL SYSTEM (REMOVE) (TEMPORARY)
0510 1 3	2	\$12,500.00	\$25,000.00	2.000	LS	N	NAVIGATION LIGHTS (PIERS)
0512 1					EA	N	NAVIGATION LIGHTS (PIERS)
0512 1 1	1	\$240,000.00	\$240,000.00	1.000	LS	N	CONTROL HOUSE (RENOVATION)
0512 71 1					EA	N	MOVABLE BRIDGE PLUMBING SYSTEM
0514 71 1	3	\$1.98	\$11,249.64	5,686.000	SY	N	PLASTIC FILTER FABRIC (SUBSURFACE)
0514 71 2	1	\$3.00	\$15,291.00	5,097.000	SY	N	PLASTIC FILTER FABRIC (STABILIZATION)
0514 72	2	\$5.09	\$302,700.00	59,424.000	SY	N	LINER IMPERMEABLE PVC
0515 1 1					LF	N	PIPE HANDRAIL (STEEL)
0515 1 2	19	\$25.80	\$368,507.31	14,284.000	LF	N	PIPE HANDRAIL (ALUMINUM)
0515 1 3	1	\$7.00	\$11,753.00	1,679.000	LF	N	PIPE HANDRAIL (STEEL, BRIDGE)
0515 1 4	1	\$23.10	\$33,471.90	1,449.000	LF	N	PIPE HANDRAIL (ALUMINUM, BRIDGE)
0515 1 5					LF	N	PIPE HANDRAIL (PVC)
0515 2101					LF	N	PED/BICYCLE RAILING (NON-SPECIFIED) (42")
0515 2202					LF	N	PED/BICYCLE RAILING (ST ONLY) (54")
0515 2301	1	\$90.00	\$645,570.00	7,173.000	LF	N	PED/BICYCLE RAILING (ALUMINUM ONLY) (42")
0515 2302					LF	N	PED/BICYCLE RAILING (ALUM ONLY) (54")
0515 2303	1	\$160.00	\$145,280.00	908.000	LF	N	PED/BICYCLE RAILING (ALUMINUM ONLY) SPE
0518 70					SY	Y	PAVT OVERLAY FABRIC
0519 71	1	\$97.00	\$23,959.00	247.000	SY	N	TRENCH DRAIN
0519 76 1					SY	Y	PRECAST CONCRETE PAVERS (ROADWAY)
0519 76 2					SY	Y	PRECAST CONCRETE PAVERS
0519 78	3	\$193.07	\$10,811.67	56.000	EA	N	BOLLARDS
0519 82					SY	N	CONC-GRASS PAVING GRID SYSTEM

# HANDRAIL PH VI

1 Bot CULVERT 259 191  
2 RAIL

LT  
RT

55' ✓ 44 MEAS  
52' ✓ 46 MEAS  
112

1 Bot CULVERT 199+35

LT  
RT

75' ✓ 59 MEAS  
68' ✓ 51 MEAS

GRAVITY WML SR 417

274+25

272+27

1 98

200 205 MEAS

PH VI = 453 TWO RAIL

PH VI 50'  
+ 100  
150

MODIFICATIONS  
THREE RAIL

PH VI 244'  
+ 200'  
444 Bot culverts  
Gravity

30'  
110  
150

# BERGERON

LAND DEVELOPMENT

15

2710 Michigan Avenue  
Kissimmee, FL 34744  
Office (407) 932-1610  
Fax (407) 932-0465

Human Resources: (407) 518-4954  
Maintenance: (407) 518-0133

June 3, 2003

URS Corporation  
1520 Tropic Park Drive  
Sanford, FL 32773

Re: Seminole County FC-1142-00/BCJ  
CR-427 Phase V & VI  
(SR 600/US 17-92 to 417 Expressway)

Attn: Charles J. Sukanek P.E.

Subject: **Adjust Contract Time - Hester Ave.**

Dear Sir,

Previously, a change order was written to provide an 8" FM from the new main on the north side of CR 427 going south along Hester Ave. At the time of construction, BLD was uncertain of how this activity would effect the overall construction schedule. Researching BLD timelines and what activities had a detrimental effect on the project completion, BLD realizes that days should have been requested for the new FM at Hester Ave. At this time, BLD requests 14 days be added to the contract for this work. If you should have any questions on this matter, please feel free to contact me.

Sincerely,  
Bergeon Land Development, Inc.

  
Carmine Resino  
Project Manager

BLD/124/Ltr133

RECEIVED

JUN - 2 2003

URS - SANFORD  
CR 427 OFFICE

May 30, 2003

Carmine Restino  
Bergeron Land Development  
5475 N. CR-427  
Sanford, FL, 32773

RE: Seminole County Road 427, Phase V and VI  
Seminole County Project FC-1142-00/BJC  
Subject: Adjustments to Contract Time for the Effects of Inclement Weather  
April 2003  
URS Letter: 0240

Dear Mr. Restino:


The daily reports documenting the effects of inclement weather on critical work and the normal seasonal weather pattern have been evaluated for the period beginning April 1 through April 30, 2003. It has been determined that 1 calendar day meets the criteria established by the contract for granting additional contract time due to the effects of inclement weather. By application of FDOT weather factors and rounding to the nearest whole number, applying any carry over from the previous time extension letter, it has been determined -0- contract days will be added to the total authorized contract time.

1	(calendar days) x 1.17 (factor)	= 1.17
-0-	(calendar days) x 1.40 (factor)	= -0-
- .30	(carryover from previous letter)	= .87
1	(contract days) granted this time period.	
Dates effected: April 9, 2003		

Your company has ten (10) days from receipt of this notice to appeal the number of days granted herein. Any such appeal must be accompanied by all available specific facts that support your position. Failure to make an appeal or to provide the specific facts supporting your position within the ten (10) days from receipt of this notice shall constitute a waiver of any rights to appeal the County's decision at a later date.

SINCERELY,

URS CORPORATION

  
Charles J. Sukanek, P.E., FOR  
Resident Engineer

CJS/jjc

CC: Jim Pullen/Steve Krug  
File

Seminole County Engineering

URS Corporation  
1520 Tropic Park Drive  
Sanford, FL 32773  
Tel: 407.324.4830  
Fax: 407.324.3811

# BERGERON

LAND DEVELOPMENT

**15**

2710 Michigan Avenue  
Kissimmee, FL 34744  
Office (407) 932-1610  
Fax (407) 932-0465

Human Resources: (407) 518-4954  
Maintenance: (407) 518-0133

May 27, 2003

URS Corporation  
1520 Tropic Park Drive  
Sanford, FL 32773

Re: Seminole County FC-1142-00/BCJ  
CR-427 Phase V & VI  
(SR 600/US 17-92 to 417 Expressway)


Attn: Charles J. Sukanek P.E.

Subject: **Memorial Day Observance**

Dear Sir,

BLD plans to shut down construction activity on the above referenced project from 3:30 p.m. Friday, May 23, 2003 until 7:00 a.m. Tuesday, May 27, 2003. As per contract specifications, BLD requests no contract time be changed for this holiday observance. If you should have any questions on this matter, please feel free to contact me.

Sincerely,  
Bergeron Land Development, Inc.



Carmine Restino  
Project Manager

**RECEIVED**

MAY 27 2003

URS - SANFORD  
CR 427 OFFICE

BLD/124/Ltr125

# BERGERON

LAND DEVELOPMENT

15

2710 Michigan Avenue  
Kissimmee, FL 34744  
Office (407) 932-1610  
Fax (407) 932-0465

Human Resources: (407) 518-4951  
Maintenance: (407) 518-0133

June 13, 2003

URS Corporation  
1520 Tropic Park Drive  
Sanford, FL 32773

Re: Seminole County FC-1142-00/BCJ  
CR-427 Phase V & VI  
(SR 600/US 17-92 to 417 Expressway)

Attn: Charles J. Sukanek P.E.

Subject: 4th of July Holiday Emergency Contacts

Dear Sir,

BLD will be shutting the above referenced job down July 4,5,6 in observation of the Independence Day holiday. As per contract specifications, BLD requests no contract time be changed for this holiday observance. The emergency contact personnel for the holiday weekend are as follows:

1. Billy Mann, Project Superintendent  
cell (407) 709-4530, home (407) 568-0187
2. Jamie Cooper, MOT Foreman  
cell (407) 908-5391
3. Turk Morrisson, Road Foreman  
cell (407) 908-5964, home (407) 892-5605
4. Carmine Restino, Project Manager  
cell (407) 908-5892, home (407) 294-7832

RECEIVED  
JUN 13 2003

URS - SANFORD  
CR 427 OFFICE


BLD/124/Ltr136



If you should have any questions on this matter, please feel free to contact me.

Sincerely,

Bergeron Land Development, Inc.



Carmine Restino  
Project Manager

Item  
Description Additional Time and Money to  
Close-Out Project CR427

	Bergeron Days	Bergeron Money	URS Days	URS Money
Lt 118 MOT Flea World	4	\$0.00	4	\$0.00
Lt 119 Limerock Trucking	8	\$3,714.00	0	\$0.00
Lt 120 SR417 MOT	28	\$4,489.75	28	\$0.00
Memorial Holiday	3	\$0.00	3	\$0.00
4th Of July Holiday	3	\$0.00	3	\$0.00
Lt 130 Sunland Repair	3	\$3,325.58	3	\$3,120.47
Lt 128 Eldreberry Driveway	2	\$1,420.11	2	\$1,274.25
Misc. Rain (May)	2		1	
Etch Traffic Seperator	3		3	
Lt 133 Hester FM	14		14	
Total	70	\$12,949.44	61	\$4,394.72
Difference			9	-\$8,554.72
Agreed Total			61	\$4,394.72

MAY 30  
JUNE 30  
July 31  
30  
31  
> 61 may

final July 31  
submit to June 30

OK  
COK  
6/5/03

RECEIVED

JUN 10 2003

URS - SANFORD  
CR 427 OFFICE
